

# Facilities Weekly Report

Volume II, Issue 52

Week of June 29-July 03, 2015

## Impact Early College

### Marshall Construction:

The ceiling grid in the hallway of the Administration Building has been installed along with the new door frames.

### Non Bond

T. Ortman– Project Inspector

### In this issue:

Impact Early College	Cover
Carver Awning	2
STEM Labs	3
MEP Bid Pkg #2 and #3	4
MEP Bid Pkg #2 and #3 Continued	5
MEP Bid Pkg #2 and #3 Continued	6
Pending Projects	7



## Carver Awning

### AVAdex Construction:

The bus awning at Carver Elementary is being installed, and the front awning is under construction.

### Bond

T. Ortman– Project Inspector



## STEM Labs

Basic I.D.I.Q., Inc.:



Demolition of ceiling tiles at Highlands Junior is underway.



Demolition and cleanup at Horace Mann has taken place.



Demolition of cabinets at Highlands Junior has been completed.

### Bond

C. Burg- Project Inspector

### MEP Bid Package #2 and #3

#### DeZavala, Harlem, and Highlands Elementary

At DeZavala, Harlem, and Highlands Elementary, all but three of the fan coil units have been set and all of them have been connected electrically . Piping modifications to connect the FCU's continue at all three schools. Air handlers continue to be removed and the new ones are being set in place. All of the new MCC's have been installed, electrical panels are being demolished, and new ones are being installed. Chilled water pumps have been replaced at two of these three schools and the old ones have been removed at the third school. The boilers at all three schools have been removed.



Moving air handler to gym mezzanine at Harlem



Preparing to lift air handler in mechanical room at Harlem



New panel being installed at Harlem



Old boiler removed at DeZavala

## MEP Bid Package #2 and #3 Continued

### Other Schools:



Air handlers at Hopper have been set on housekeeping pads.



New electrical conduit was installed at Austin



New chilled water pumps and piping have been installed at Austin.




This room is awaiting new air handlers at Ashbel Smith.

## MEP Bid Package #2 and #3 Continued

### Other Schools:



RTU being removed from gym roof at Baytown Junior.

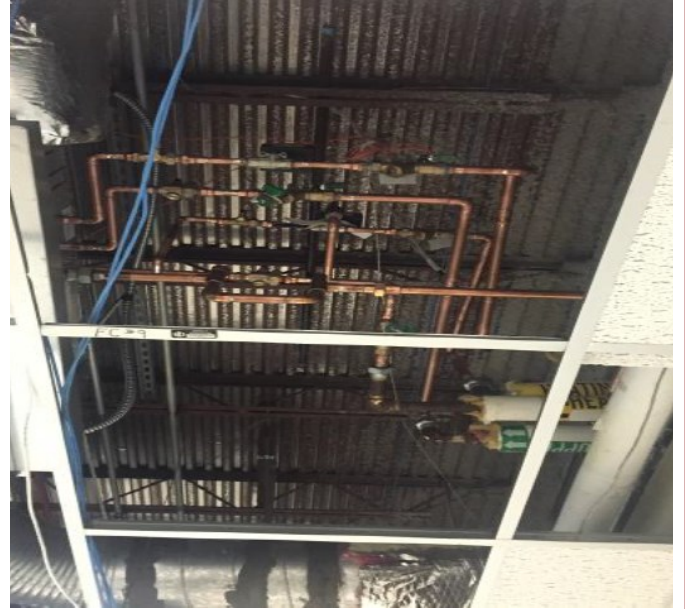

New piping for FCU's at Horace Mann.

### Administration Building

Phase 3A of the work at the Administration Building is nearing completion. Floor protection for phase 4A is underway.

### Bond

C. Burg- Project Inspector

Facilities Planning & Construction  
3401 N. Main  
Baytown, Texas 77521

Phone: 281-425-3600

Fax: 281-420-5140

E-mail: dkfluker@gccisd.net

**Staff**

...

**Executive Director:**

David Fluker

**Asst. Director:**

Brenda Garcia

**Project Manager:**

Bruce Riggs

**Senior Project Inspector:**

Ray Brown

**Project Inspectors:**

Carl Burg

Tom Ortman

**Pending Projects:**

- Data Center <sup>B</sup>  
-The schematic design is scheduled for presentation to Board of Trustees on July 13th.
- GCM Wing Addition <sup>B</sup>  
-The bid schedule is being set.
- Natatorium <sup>B</sup>
- Stallworth Handrails  
-The contractor is scheduling materials and work.
- Stuart/Kilgore Repurpose <sup>B</sup>  
-The schematic design is scheduled for presentation to Board of Trustees on July 13th.
- Transportation Center <sup>B</sup>
- Travis Parking <sup>NB</sup> (Not Funded)

B- Bond

NB- Non Bond

