

# Facilities Weekly Report


Volume II, Issue 56

Week of July 27-31, 2015

## MEP Bid Package #2 and #3

### Prime Contractors, INC:

All piping to the new FCU's at **Horace Mann** have been insulated. Water has circulated and AC is in the process of starting up.

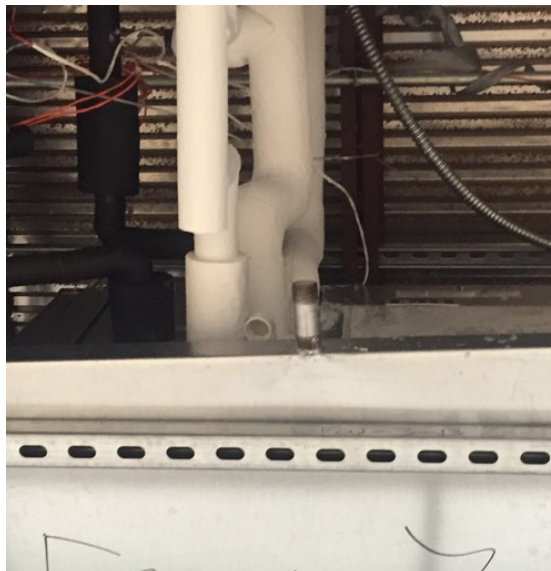

All roof top units at **Baytown Junior** have been set.


### In this issue:

MEP Bid Pkgs #2 & #3	Cover
MEP Bid Pkgs #2 & #3 Continued	2
MEP Bid Pkgs #2 & #3 Continued	3
Bañuelos Signal Light	4
Pending Projects	5



The new MSB at **Gentry** has been installed.

### MEP Bid Package #2 and #3 Continued

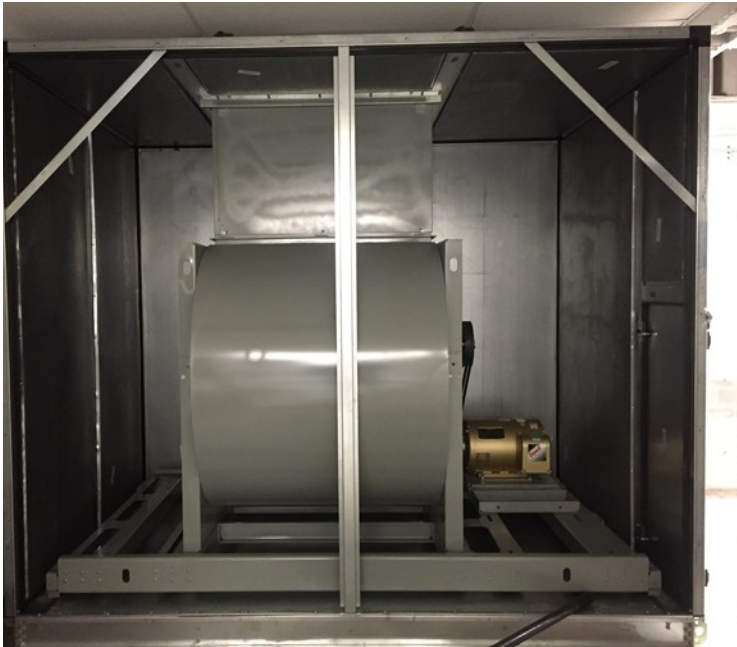

The air handler is ready to move into the mechanical room at **Cedar Bayou Junior**. Both new units have been set and are awaiting piping and ducting.



The new MSB at **DeZavala** has been installed.



Piping for new boilers at **Horace Mann** have been insulated.



All of the new AHU's at **Ashbel Smith** have been piped and insulated. AC expected to start up by Friday, July 31st.



## MEP Bid Package #2 and #3 Continued



The new chillers at **Ashbel Smith** were delivered. They have been set and are now being piped.



A temporary chiller is being set up at **Austin**. AC system is up and running as of Friday, July 24th. The new chiller is to be delivered on August 24th and will be set over the labor day weekend.

### **Bond**

C. Burg– Project Inspector



The new MSB at **San Jacinto** is being set up.

## Bañuelos Signal Light

### Marshall Construction:

Traffic signal wiring is being installed at the northwest and northeast corners of Garth and Seabird intersection. Excavation work for the concrete sidewalk has begun.

### Bond

Ray B.--Senior Project Inspector





Facilities Planning & Construction  
3401 N. Main  
Baytown, Texas 77521

Phone: 281-425-3600

Fax: 281-420-5140

E-mail: dkfluker@gccisd.net

**Staff**

...

**Executive Director:**

David Fluker

**Asst. Director:**

Brenda Garcia

**Project Manager:**

Bruce Riggs

**Senior Project Inspector:**

Ray Brown

**Project Inspectors:**

Carl Burg

Tom Ortman

**Pending Projects:**

- Data Center<sup>B</sup>  
-The design development phase is underway.
- GCM Wing Addition<sup>B</sup>  
-The bid schedule is being set.
- Natatorium<sup>B</sup>
- Stallworth Handrails  
-The contractor is scheduling materials and work.
- Stuart/Kilgore Repurpose<sup>B</sup>  
-The design development phase is underway.
- Transportation Center<sup>B</sup>
- Travis Parking<sup>NB</sup> (Not Funded)

B- Bond

NB- Non Bond

