

Facilities Weekly Report

Volume II, Issue 24

Week of March 17-21, 2014


Johnny T. Clark

Marshall Construction:

They have started installing metal stud framing on the canopy. The face brick installation has begun. The front parking lot, entrance driveway, and concrete curb have been poured. The metal stud framing on the MEP rough-in has begun as well. Lastly, the insulation and drywall has begun on both sides of the walls.

Bond

R. Brown-Senior Project Inspector

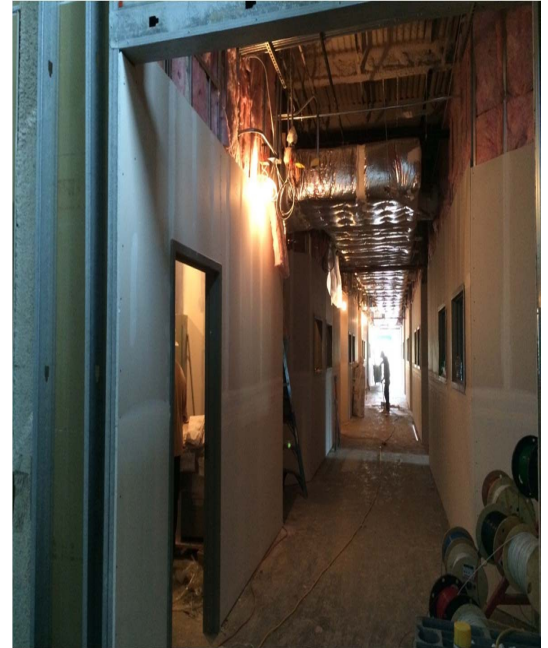

Inside this issue:

New Elementary on Eastpoint 2

RSS Baseball Canopies 2

RSS Parking lot 3

RSS Kluch Entrance 3


New Alamo Elementary

Marshall Construction:

They are installing the metal stud framing on the canopies. The face brick on the east wall is being installed. Insulation and drywall installation has begun as well. The sealant on the HVAC ducts has been applied. The supply and return chilled water piping to the pumps and boilers are also being set in place.

Bond

R. Brown-Senior Project Inspector

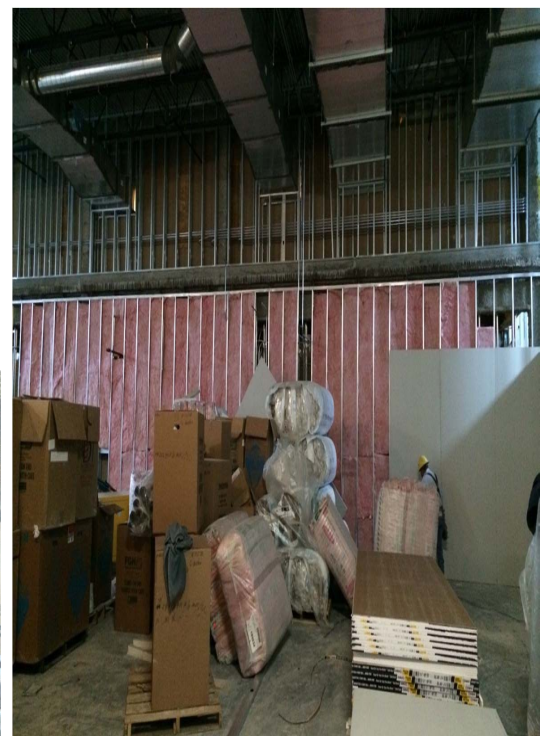

Bañuelos Elementary

Marshall Construction:

They have begun with tile work and drywall installation in the bathrooms. Equipment is being installed in the mechanical room and skylights are being installed as well.

Bond

R. Brown-Senior Project Inspector



RSS Softball Batting Cage Awnings

AvAdek:

They have completed the framing of the boys' baseball canopy. They also have started the installation of the R-panel covering.

Non-Bond

T. Ortman-Project Inspector



RSS Parking Lot

G.W. Phillips Construction:
Due to bad weather, there were delays in finishing the scheduled concrete placement of the sidewalks. This needed to be completed before continuing with re-grading the soccer fields.

Non Bond

B. Garcia-Project Inspector




Kluch Entrance at RSS

General Construction:
With the majority of the work completed on the entrance, a few items are left to be addressed. The lettering to be placed on the steel beam has been ordered, and upon its installation the project will be complete.

Bond

T. Ortman-Project Inspector

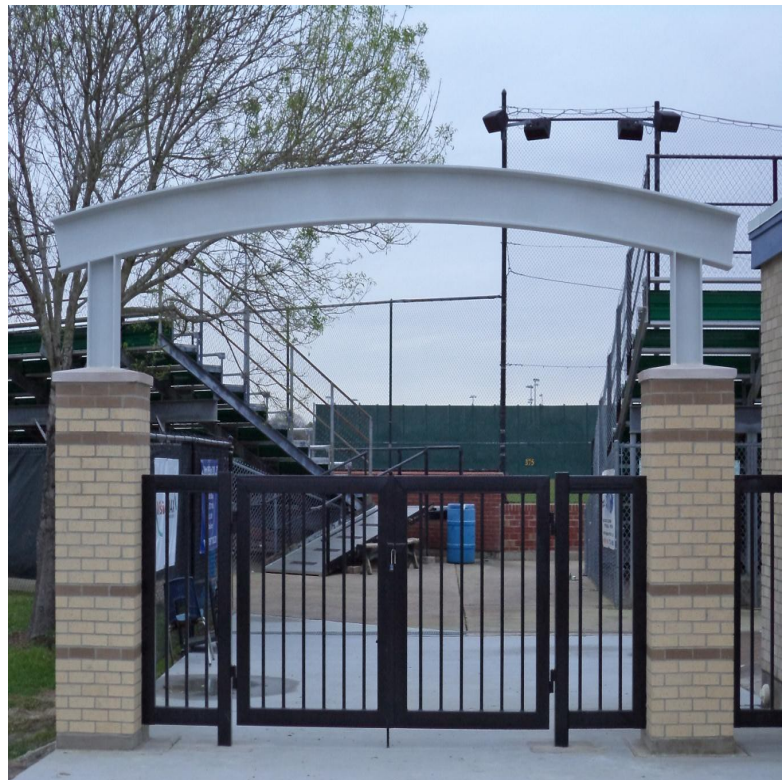

BOND & NON BOND

Facilities Planning & Construction
3401 N. Main
Baytown, Texas 77521

Phone: 281-425-3600
Fax: 281-420-5140
E-mail: dkfluker@gccisd.net

Pending Projects

Impact Early College High School - Final construction drawings are at the City of Baytown for approval. The CM@R contract is currently under negotiations.

