

# Facilities Weekly Report

Volume II, Issue 32

Week of May 12-16, 2014

## Johnny T. Clark

### Marshall Construction:

Installation of the light poles in the parking lot is taking place. The front canopy is being finished up including the waterproofing and cast stone column installation. The rotunda/main lobby, wall tile installation and drywall tape and float are being done, as well as the vestibule, taping and floating. Electrical wiring installation throughout and prime painting has begun. In some corridors, floor prep has started for the floor tile installation to begin. Kitchen roof installation of the final roof membrane is also taking place. Excavation is being done for conduits from MDF to pull box on street for telecom services.

### Bond

R. Brown-Senior Project Inspector



### Inside this issue:

New Alamo Elementary 2

Bañuelos 3

Crockett Elementary 4

Sterling High School 4

## New Alamo Elementary

### Marshall Construction:

They are placing concrete for the circular playground area, and priming and painting the walls throughout. The final layer of the roof membrane has been installed, as well as the roof over the kitchen area.

### Bond

R. Brown-Senior Project Inspector




## Bañuelos Elementary

### Marshall Construction:

Grading and stabilizing for the entrance driveway has begun. Floor tile has started being placed in the corridors throughout the campus. The final layer of the roof membrane has been installed and the roof drain strainer has been installed as well.

### Bond

R. Brown-Senior Project Inspector

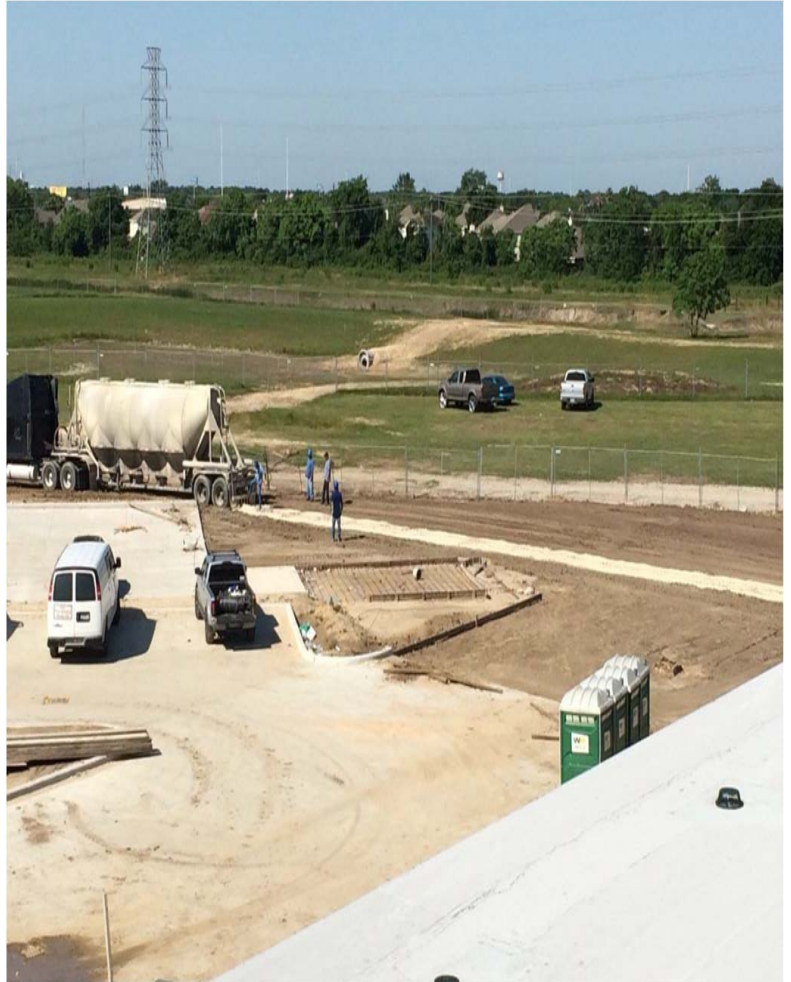

### Crockett Parking lot

**Horizon:**

The conduit, that will be used to supply the new marquee, was located and marked. The marquee will be located near the new parent entrance along Blue Herron Road.

**Non-Bond**

B. Garcia: Project Inspector



### Sterling Parking Lot

**G.W. Phillips Construction:**

The dirt that was trucked in began to be re-distributed at the soccer fields. This was the first step in regrading both fields.

**Non-Bond**

B. Garcia: Project Inspector



## BOND & NON BOND

Facilities Planning & Construction  
3401 N. Main  
Baytown, Texas 77521

Phone: 281-425-3600

Fax: 281-420-5140

E-mail: [dkfluker@gccisd.net](mailto:dkfluker@gccisd.net)

## Pending Projects

**Impact Early College High School** - Still under permit review.

**Transportation Center**– Planning stages.

**GCM Wing Addition**-Contract negotiations.

**Technology Data Center**-Contract negotiations.

**Security Projects**-Planning Stages.

**Life Safety**-Seeking proposals.

