

Facilities Weekly Report

Volume II, Issue II

Week of October 28-November 1, 2013

New Elementary - Hwy 146

Marshall Construction canceled all slab concrete pours last week due to heavy rain. Re-compacting the soil prior to the next concrete pour. Lime was used to aid in drying out the soil.

Bond

R. Brown-Senior Project Inspector



Inside this issue:

New Elementary on Eastpoint 2

Crockett Parking Lot and Drive 3

RSS Natatorium 3

Robert E. Lee Parking Lot and Drive 3

New Alamo Elementary - N. Main

Marshall Construction has completed structural steel in the Pre-K, all the classrooms, administrative offices and the library. Fabricated steel joists are due to arrive next week.

Bond

R. Brown-Senior Project Inspector




New Elementary - Eastpoint

Marshall Construction has finished the concrete pour for the emergency turnaround and visitor's parking area before the heavy rains hit. Structural steel erection continues.

Bond

R. Brown-Senior Project Inspector

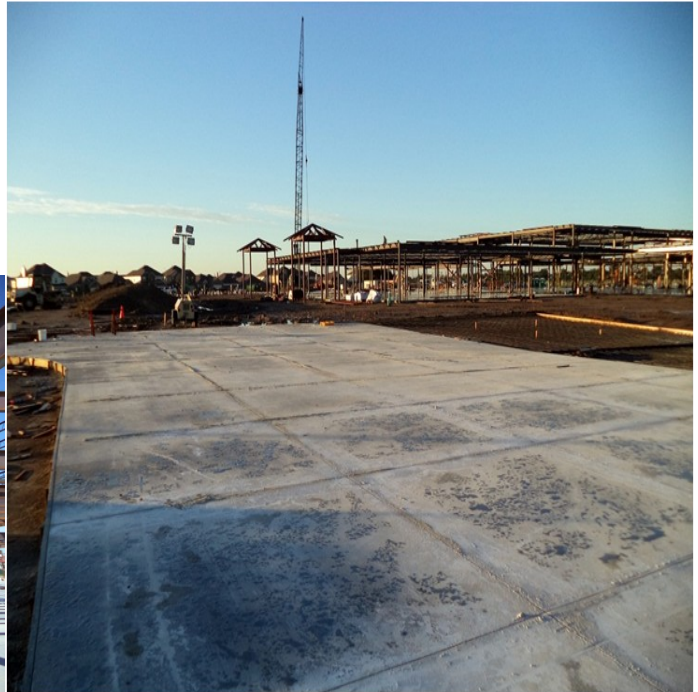

Crockett Parking Lot and Drive

Horizon has been clearing shrubs and small trees to prepare for the installation of fencing along the new Blue Heron Dr. Conduit work for access control was completed at the future parent drive entrance.

Non Bond

B. Garcia-Project Inspector



RSS Natatorium

Chatham Construction, the contractor for the RSS Natatorium job, is replacing old plywood material around the pool with new Trex decking.

Non Bond

T. Ortman-Project Inspector



Robert E. Lee Parking Lot and Drive

Horizon has had the first pour for the parking lot, approximately 690 yards of concrete in one quadrant. The concrete pour was placed via a large pump truck. The second half of the parking lot was prepared for the next pour over the weekend.

Bond

B. Garcia-Project Inspector



BOND & NON BOND

Facilities Planning & Construction
3401 N. Main
Baytown, Texas 77521

Phone: 281-425-3600
Fax: 281-420-5140
E-mail: dkfluker@gccisd.net

Pending Projects

Ross S. Sterling North Parking - The contract with G. W. Phillips was approved by the Board of Trustees on October 28, 2013. Work is being scheduled.

Sterling; Ronnie Kluch Entrance— General Construction Company contract will go to the Board of Trustees on November 11 for approval.

Impact Early College High School - PBK commences designing.

Program Management— RFQ bids were accepted and evaluated and will go the Board of Trustees on November 11, 2013 for approval.

