

# Facilities Weekly Report

Volume II, Issue 14


Week of December 2-6, 2013

## New Elementary - Hwy 146

Marshall Construction will continue with roof decking and final slab on grade concrete placement. Structural steel will complete in three weeks with canopy to follow.

### Bond

R. Brown-Senior Project Inspector

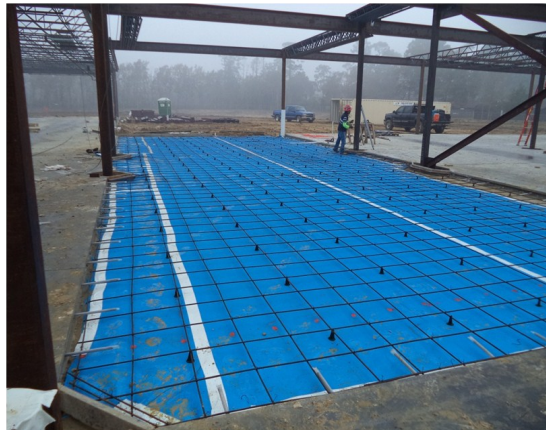

### Inside this issue:

New Elementary on Eastpoint 2

Venthoods 2

Crockett Parking Lot and Drive 3

RSS Natatorium 3

Robert E. Lee Parking Lot and Drive 3

## New Alamo Elementary - N. Main

Marshall Construction has completed main building steel erection and started the canopy framing at entrance. Staff parking and bus drop off paving is 85% complete.

### Bond

R. Brown-Senior Project Inspector



### New Elementary - Eastpoint

Marshall Construction has completed roof decking and lightweight concrete roof fill is underway. Staff parking paving is nearing completion.

**Bond**

R. Brown-Senior Project Inspector



### RSS Parking lot

G. W. Phillips has been working on the RSS parking lot preparing for a Athletic parking lot.

B. Garcia-Project Inspector



## Crockett Parking Lot and Drive

Horizon has continued work with the remainder of the curbs and mow strip at the parent drive. In addition the fencing at the front of the school is progressing. CMU blocks have been installed in preparation for the brick work.

**Non Bond**

B. Garcia-Project Inspector



## RSS Natatorium Phase II

Upgrade of finishes, seating, lights, and fans being priced at this time.

**Non-Bond**

T. Ortman-Project Inspector



## Robert E. Lee Parking Lot and Drive

Over the Thanksgiving holidays, Horizon pours a large portion of the drive. Work also continued on electrical conduit in the parking lot area.

**Bond**

B. Garcia-Project Inspector



## BOND & NON BOND

Facilities Planning & Construction  
3401 N. Main  
Baytown, Texas 77521

Phone: 281-425-3600  
Fax: 281-420-5140  
E-mail: [dkfluker@gccisd.net](mailto:dkfluker@gccisd.net)

## Pending Projects

**Ross S. Sterling North Parking** - Preparation of sub-grade is underway.

**Sterling; Ronnie Kluch Entrance**- The contract with General Construction Company will go before the Board of Trustees on December 16, 2013.

**Impact Early College High School** - PBK preparing design and development documents for Board presentation on December 16, 2013.

**Program Management**- The contract with Lockwood, Andrews & Newman, Inc. for the program management will go before the Board on December 16, 2013.

