



# Intermittent Report

August 5, 2021

## Index

E.F. Green JS	Cover
MEP #1 at Sterling HS	Cover
Stuart CTHS Phase 4	2
JS Running Tracks	2
San Jacinto ES	3
Pumphrey ES	3
Projects' Status	4

## E.F. Green J.S.

### Project Notes:

- Gym flooring installation underway
- Final clean in Academic Building is in progress
- Flat work at central courtyard is nearly complete
- Installation of classroom furniture is in progress
- Install of sod at football field is complete



Floor polish complete at cafeteria

Pfluger

Pogue Construction

## MEP #1 at Sterling H.S.

### Project Notes:

- Tile installation in restrooms is ongoing
- Insulating ductwork and hydronic piping at choir area is underway
- Installation of conduit and speaker wire in choir area is in progress
- Installation of fire sprinkler lines in choir area is ongoing



Scaffolding removed in auditorium

GCCISD  
Facilities Planning and  
Construction

LAN  
Program Managers




EMA Engineering

## SCTHS Phase 4

### Project Notes:

- Final cleaning in building is underway
- Site clean-up is near completion
- New building furniture installation scheduled to begin next week
- Project has been issued a Temporary Certificate of Occupancy by the City of Baytown

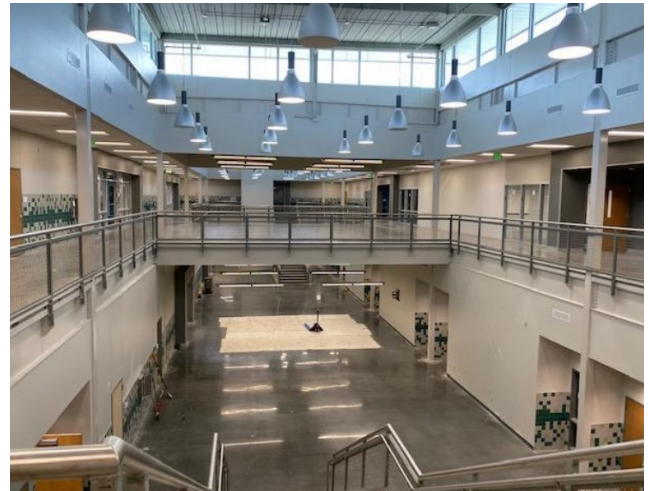

**Atrium Area Overview**

**Pfluger**

**Pogue Construction**

## Junior School Running Tracks

### Project Notes:

- Sod installation is complete at Horace Mann JS and Gentry JS
- Sod is scheduled to be installed at Highlands JS by the end of next week
- New fire lane is complete at Cedar Bayou JS and track curb installation continues
- Contractor schedule to mobilize at Baytown JS once complete at Highlands JS



**Aerial view at Highlands Junior**

**PBK Sports**

**Athletic Field Specialists**

## San Jacinto Elementary School

### Project Notes:

- Exterior waterproofing is underway along building perimeter
- Installation of mechanical, electrical, and plumbing system continues throughout
- Hydronic piping assembly and installation is in progress
- Lightweight concrete installation is complete at roof
- Metal framing installation in underway



**Mechanical duct hanging is ongoing**


**PBK**

**Marshall Construction**

## Jessie Lee Pumphrey Elementary School

### Project Notes:

- Exterior waterproofing is complete along cafeteria perimeter, brick veneer is underway
- Installation of mechanical, electrical, and plumbing system continues throughout
- Hydronic piping assembly and installation is in progress
- Lightweight concrete installation is complete at roof
- Metal framing installation in underway

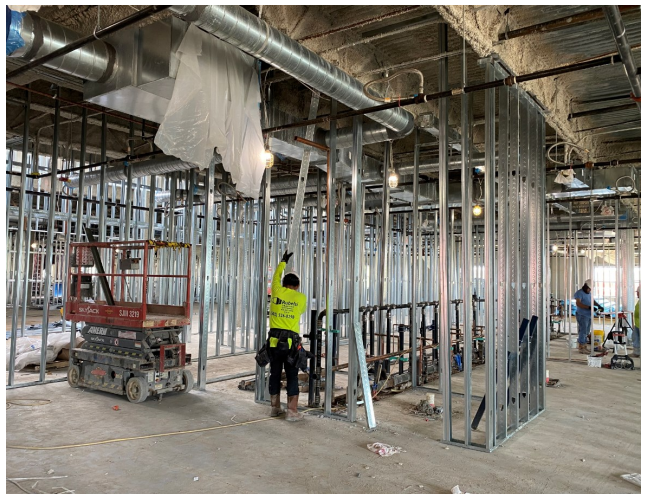

**Plumbing top-out is ongoing**

**PBK**

**Drymalla Construction**

## Projects' Status

### CTE Sterling HS Construction Lab Renovation

- Mechanical/Electrical/Plumbing systems installation is nearing completion
- New Epoxy flooring is scheduled to be installed next week
- New dust collection system installation is nearly complete
- Finishes and millwork are schedule to be complete by end of next week

### Education Service Center - Phase 1C

- New HVAC system is complete
- Tape and floating of gypsum is complete
- First coat of paint is underway
- Furniture is scheduled to be delivered by 8/16

### Districtwide Roof Replacement

- Installation of new roof system continues at Gentry Junior School and Baytown Junior School
- Roof work will progress through the first few months of the new school year

### Lee High School & Gentry Junior School Fine Arts Project

- Project is currently in Construction Documents Phase
- 50% plan review is scheduled for late August, with a completion date in late September

