

# Facilities Weekly Report

Volume II, Issue 57

Week of August 3-7, 2015

## Data Center

### Raba Kistner Consulting:

Work has started on the geotechnical soil sampling needed for the structural design of the building, parking lots, and driveways.

### Bond

Ray B.—Senior Project Inspector

### In this issue:

Data Center	<b>Cover</b>
MEP Bid Pkgs #2 & #3	<b>2</b>
MEP Bid Pkgs #2 & #3 Continued	<b>3</b>
Bañuelos Signal Light	<b>4</b>
Lee High School Window Replacement	<b>5</b>
District Wide Elevator Repair	
Bowie and Travis Awning	<b>6</b>
Lamar Roof	
Impact Early College	<b>7</b>
STEM Labs	
Pending Projects	<b>8</b>



## MEP Bid Package #2 and #3

Prime Contractors, INC:



The air handler piping is has been completed at **Cedar Bayou**, along with insulation and ducting.



The new MSB at **Horace Mann** has been installed.



The new distribution panel is being installed in the **RSS Ag Science** building.



The new MSB at **Crockett** is waiting on city inspection for August 4th.

### MEP Bid Package #2 and #3 Continued



The new AHU piping and ducting have been connected at **Hopper**.



The new condenser water piping is being installed at **San Jacinto**.

**Bond**  
C. Burg– Project Inspector



The DX unit at **Cedar Bayou** Special Education Building has been set.

The AC is running at Ashbel Smith, Lamar, Highlands Elem., Hopper, Horace Mann, Harlem, Gentry, and Baytown Junior to debug the systems. Controls at all campuses are working.

## Bañuelos Signal Light

### Marshall Construction:

The signal light heads are in the process of being installed and wired. The meter pole, meter base and disconnect have been installed. Inspection has been called for and will be followed by CenterPoint providing power.

### Bond

R. Brown- Senior Project Inspector



## Lee High School Window Replacement

### Comex:

The final shipment of window glass has arrived and all of the double window configuration are now being installed. Replacement of the windows will continue until school starts, then the contractor will work on the evenings and weekends until the project is completed.

### Bond

R. Brown- Senior Project Inspector



## District Wide Elevator Renovations

### KONE Inc.:

Work continues at Ashbel Smith, Horace Mann, Sterling Annex, and Sterling Commons Elevators have been completed and inspected at Administration, San Jacinto, Lee Science, Lee Cafeteria, and Lee 400 building. The Lee Office, Horace Mann and Ashbel Smith are in the next group to be inspected next week.

### Bond

R. Brown- Senior Project Inspector



## Bowie and Travis Awning

### AVAdex Construction:

The Bowie awning is being installed in front of the campus and is almost complete. The Travis awning is complete.

### Bond

T. Ortman- Project Inspector



## Lamar Roof

### Rios Construction and Roofing:

Work on the tower is just about complete.

### Bond

T. Ortman- Project Inspector




## Impact Early College

### Marshall Construction:

The serving line in the cafeteria is being installed.

### Non-Bond

T. Ortman- Project Inspector

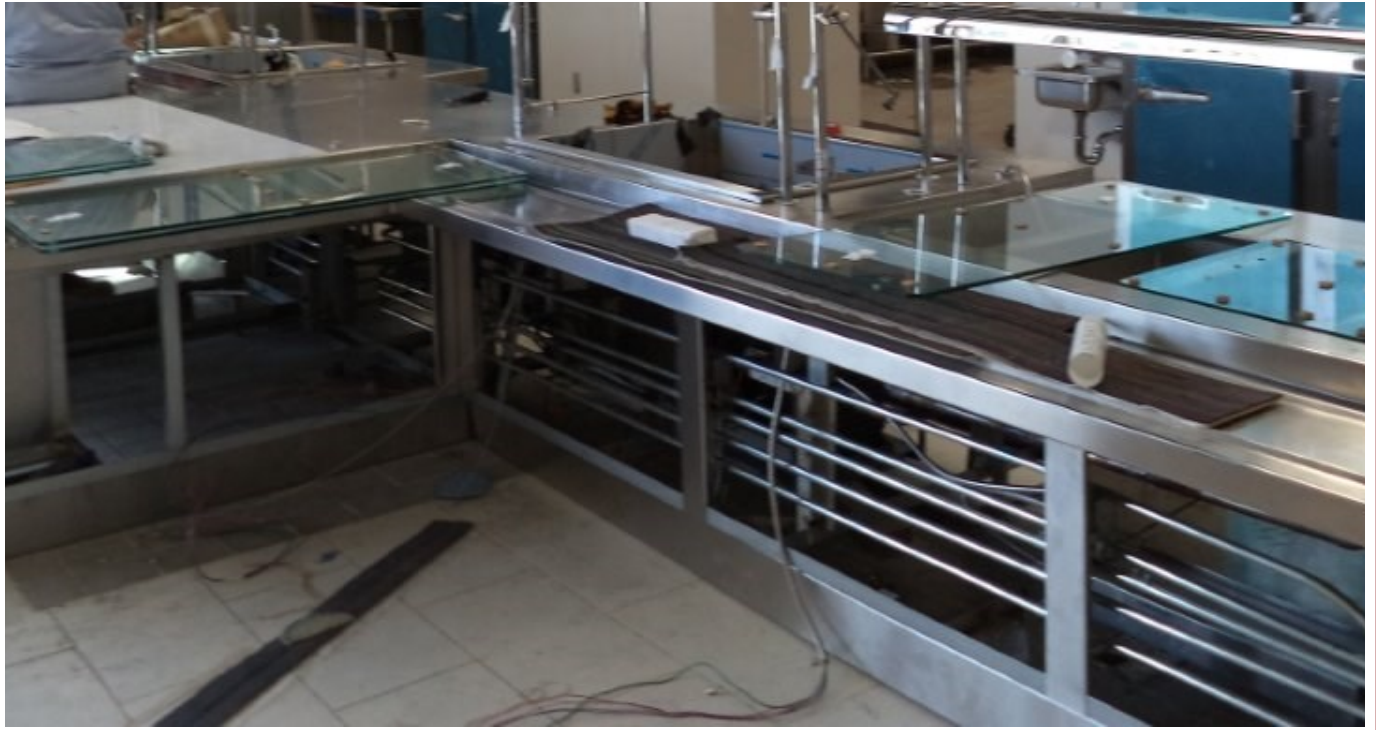


## STEM Labs

### Marshall Construction:

Baytown Junior and Horace Mann STEM Labs are set up.

### Bond

C. Burg- Project Inspector

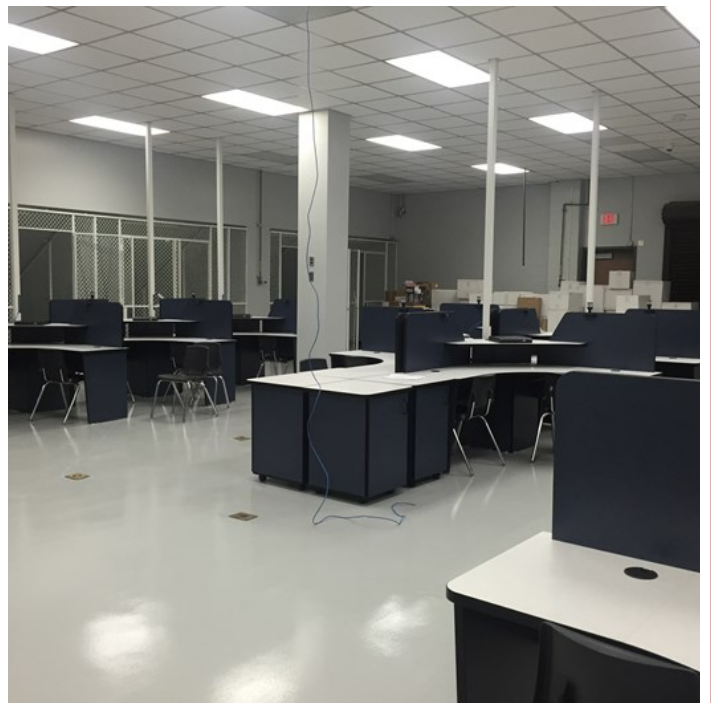

Facilities Planning & Construction  
3401 N. Main  
Baytown, Texas 77521  
Phone: 281-425-3600  
Fax: 281-420-5140  
E-mail: dkfluker@gccisd.net

**Staff**

...

**Executive Director:**

David Fluker

**Asst. Director:**

Brenda Garcia

**Project Manager:**

Bruce Riggs

**Senior Project Inspector:**

Ray Brown

**Project Inspectors:**

Carl Burg

Tom Ortman

**Pending Projects:**

- GCM Wing Addition <sup>B</sup>  
-The bid schedule is being set.
- Natatorium <sup>B</sup>
- Stallworth Handrails  
-The contractor is scheduling materials and work.
- Stuart/Kilgore Repurpose <sup>B</sup>  
-The design development phase is underway.
- Transportation Center <sup>B</sup>
- Travis Parking <sup>NB</sup> (Not Funded)

B- Bond

NB- Non Bond

