

# Facilities Weekly Report

Volume II, Issue 23


Week of March 10-14, 2014

## Johnny T. Clark

Marshall Construction had a concrete placement of 1600 cubic yards, and are preparing for another concrete placement next week, weather permitting. Storm drain piping is nearing completion followed by the detention pond modifications. Domestic water, fire lines and sanitary sewer have been completed and successfully tested.

### Bond

R. Brown-Senior Project Inspector

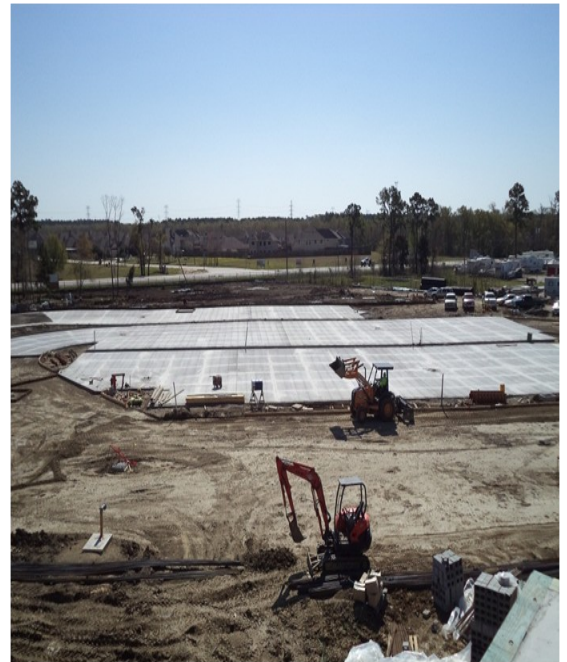

### Inside this issue:

New Elementary on Eastpoint 2

RSS Baseball Canopies 2

RSS Parking lot 3

RSS Kluch Entrance 3

## New Alamo Elementary

Marshall Construction masons are installing the face brick on the exterior. Drywall installed in the interior side, of the exterior walls. The insulation between classrooms has been installed and the hallways have also been insulated for sound. After the chilled and hot water lines have been tested, insulation of the piping will continue.

### Bond

R. Brown-Senior Project Inspector



## Banuelos Elementary

Marshall Construction has dried in the entire building and drywall has begun. Face brick installation continues on high wall in the gym/cafeteria and high corridors. Concrete block installation continues in the kitchen and mechanical areas.

### Bond

R. Brown-Senior Project Inspector



## RSS Softball Batting Cage Awnings

AvAdek has started the framing of the boys' baseball canopy located on 3rd base side. Installation of joists proceeds roof panel application.

### Non-Bond

T. Ortman-Project Inspector



## RSS Parking Lot

G.W. Phillips Construction had a concrete placement of 140 cubic yards on Saturday. Preparation for installing sidewalk scheduling.

### Non Bond

B. Garcia-Project Inspector



## Kluch Entrance at RSS

General Constuction has finished the brick columns and the steel has been painted. Also a gate has been installed. Installation of lettering on sign being scheduled.

### Bond

T. Ortman-Project Inspector



## BOND & NON BOND

Facilities Planning & Construction  
3401 N. Main  
Baytown, Texas 77521

Phone: 281-425-3600  
Fax: 281-420-5140  
E-mail: [dkfluker@gccisd.net](mailto:dkfluker@gccisd.net)

## Pending Projects

**Impact Early College High School** - Final construction drawings due next week.  
CM@R proposals have been evaluated and will go to the board for approval on March 24, 2014.

