

# Facilities Weekly Report

Volume II, Issue 26

Week of March 31-April 4, 2014


## Johnny T. Clark

### Marshall Construction:

They are finishing on the south elevation with brick surface cleaning. Face brick is being completed as well on roof area "B." Curb support for the fan and condensing units are installed. Bus driveway is being formed and re-bar installed, as well as the staff parking lot. Concrete placement is scheduled for next week.

### Bond

R. Brown-Senior Project Inspector

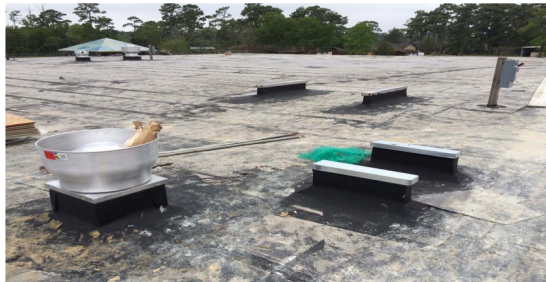

### Inside this issue:

New Elementary on Eastpoint 2

RSS Parking Lot 3

Crockett Parking Lot and Drive 4

## New Alamo Elementary

### Marshall Construction:

They are finishing all high wall face brick installation. The exhaust fans and roof hoods are being connected. Roof support curbs for fan and condensing units are being installed.

### Bond

R. Brown-Senior Project Inspector





## Bañuelos Elementary

### Marshall Construction:

They are finishing all high walls with face brick installation. The face brick installation at exterior wall of cafeteria and gymnasium is being finished. The high walls of the front lobby, including face brick, are getting final inspection. Roof hoods are being installed as well as roof access hatches.

### Bond

R. Brown-Senior Project Inspector





## RSS Parking Lot

G.W. Phillips Construction:  
After more rain delays, the forms used to pour the concrete have been wrecked and cleaned up. Backfilling has taken place. Also, the bottom channel of the detention pond was poured.

### Non Bond

B. Garcia-Project Inspector



## BOND & NON BOND

Facilities Planning & Construction  
3401 N. Main  
Baytown, Texas 77521

Phone: 281-425-3600  
Fax: 281-420-5140  
E-mail: [dkfluker@gccisd.net](mailto:dkfluker@gccisd.net)

### Crockett Parking Lot and Drive

#### Horizon:

Coordination continues to provide the new gate kiosks with phone lines and power for the card access readers. In addition, two new benches were installed at the playground area on the south side of the campus.

#### Non-Bond

B. Garcia-Project Inspector



### Pending Projects

**Impact Early College High School** - Final construction drawings are at the City of Baytown for approval. The CM@R contract is currently under negotiations.

