

Facilities Weekly Report

Volume II, Issue 27

Week of April 7-14, 2014

Johnny T. Clark

Marshall Construction:

They are installing and waterproofing the front canopy. Metal stud framing and drywall installation throughout the campus is taking place. Wall tile is being installed as well as taping and floating drywall and ceiling grid is being hung. HVAC duct work is being installed.

Bond

R. Brown-Senior Project Inspector



Inside this issue:

New Elementary on Eastpoint 2

RSS Parking Lot 3

Crockett Parking Lot and Drive 4


New Alamo Elementary

Marshall Construction:

They are finishing face brick installation on the south exterior wall of the stage. Aluminum storefront was installed at the front entrance. Metal stud framing and drywall installation in the vestibule/front lobby is taking place. Metal grid work is being installed throughout, with light installation, as well as tape and floating drywall. Tile work has begun.

Bond

R. Brown-Senior Project Inspector

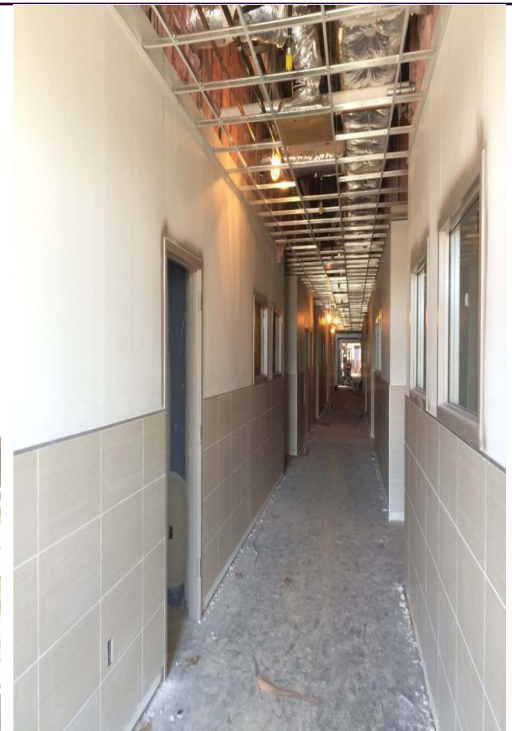

Bañuelos Elementary

Marshall Construction:

They have installed aluminum frame and bullet resistant glass on the left side of the front entrance. Drywall installation and taping and floating, as well as ceiling grid, is underway. Ceiling lights are being installed throughout the campus. Also, quarry tile is being installed in the kitchen.

Bond

R. Brown-Senior Project Inspector



REL Parking Lot

Horizon:

Power to the gates has been established. Coordination continues for the programming of the gates and for the installation of the phone line at the kiosk. The lot has been operational for parking.

Non Bond

B. Garcia-Project Inspector



Walls at Highlands Jr.

Chatham Construction:

New walls and doors are being installed in the principal's office area. Also, another wall is being constructed in the main hallway to create an additional office area.

Non Bond



BOND & NON BOND

Facilities Planning & Construction
3401 N. Main
Baytown, Texas 77521

Phone: 281-425-3600
Fax: 281-420-5140
E-mail: dkfluker@gccisd.net

Crockett Parking Lot and Drive

Horizon:

The new gated entrances have been powered up and are ready for programming. The phone lines for the kiosk entries have also been connected and are in the process of being programmed. Also, the cameras at the kiosks have been installed along with a monitor for the reception area. Cleanup has continued and the hydro-mulching has caused the grass to begin growing in.

Non-Bond

B. Garcia-Project Inspector



Pending Projects

Impact Early College High School - Final construction drawings are at the City of Baytown for approval. The CM@R contract is currently under negotiations.

