

# Facilities Weekly Report

Volume II, Issue 28

Week of April 14-18, 2014

## Johnny T. Clark

### Marshall Construction:

They are installing the face brick at the south canopy. Exterior sheathing and waterproofing is being installed at the front canopy, as well as plywood and waterproof membrane on the roof. Curbs are being poured in the bus driveway area. CMU is being installed around the chillers. Quarry tile is being installed in the kitchen and serving line areas. Lastly, the transformer has been installed, and soon there will be electricity at the school.

### Bond

R. Brown-Senior Project Inspector



### Inside this issue:

Bañuelos Elementary 2

New Alamo Elementary 3

Crockett Parking Lot and Drive 4






## Bañuelos Elementary

### Marshall Construction:

They have started the demolition of the street. Saw cutting began at the pavement on Seabird Street for the new driveway entrance to the staff parking lot/busway. Site clean-up has begun around the concrete water meter vault. The sanitary sewer manhole is on site to replace the exiting manhole the city had on the driveway. Installation of the final layer of roofing material was completed. The electrical meter and transformer was installed by Centerpoint. Power is now available in the building.

### Bond

R. Brown-Senior Project Inspector

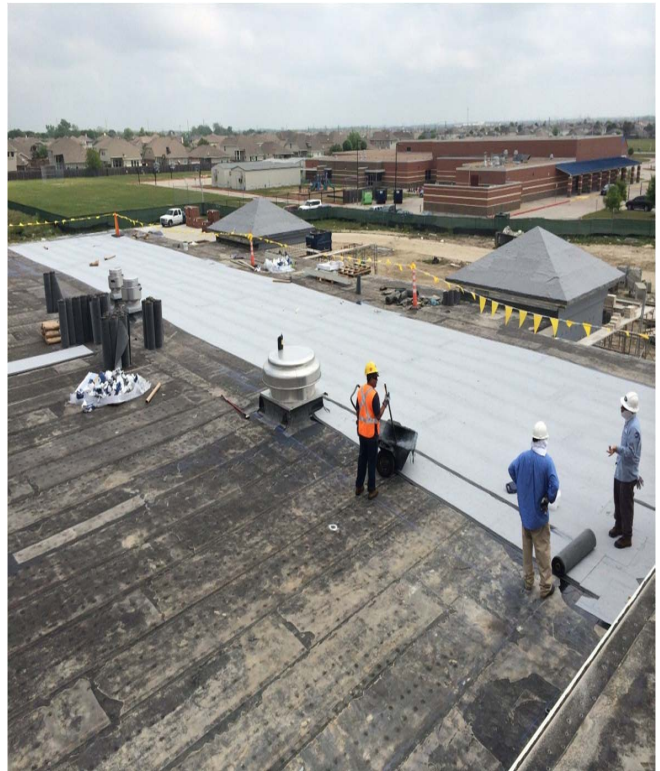




## New Alamo Elementary

### Marshall Construction:

They are working on the front canopy installing plywood and waterproof membrane on the roof. Forming up the front sidewalks along the driveway is occurring. They are working to install the perimeter flashing on the roof edges as well. And installing the quarry tile in the kitchen area, and the freezer-cooler area. Is underway. Centerpoint energy has installed the transformer and soon there will be power to the building.

### Bond

R. Brown-Senior Project Inspector

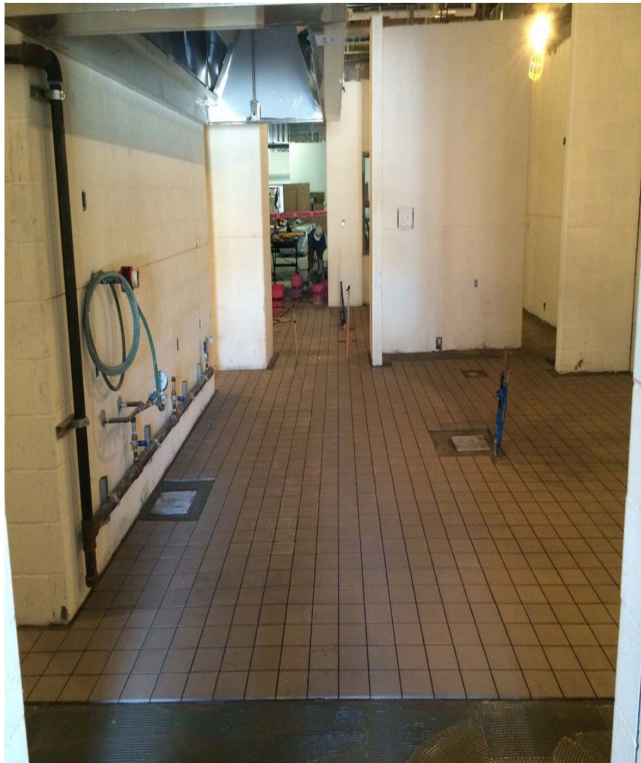

## BOND & NON BOND

Facilities Planning & Construction  
3401 N. Main  
Baytown, Texas 77521

Phone: 281-425-3600  
Fax: 281-420-5140  
E-mail: [dkfluker@gccisd.net](mailto:dkfluker@gccisd.net)

## Crockett Parking Lot and Drive

### Horizon:

A new electronic sign marquee has been ordered. It is to be placed near the new parent entry at the southeast corner of the property and can be read from either side along Blue Heron Parkway.

### Non-Bond

B. Garcia-Project Inspector



## Pending Projects

**Impact Early College High School** - Final construction drawings are at the City of Baytown for approval. This will enable a building permit to be issued to the contractor. The CM@R contract is currently under negotiations.

