

# Facilities Weekly Report

Volume II, Issue 4

Week of September 16-20,

## Inside this issue:

New Elementary on Eastpoint 2

Crockett Parking Lot and Drive 3

Portable Classrooms 3

Robert E. Lee Parking Lot and Drive 3

## New Elementary - Hwy 146

Trees are being chipped and the site is still being cleared. Also, building pad work began this week.

### Bond

D. Fluker-Executive Director



Site clearing has been completed

## New Alamo Elementary - N. Main

Work is focused on completing drilled piers in preparation for grade beam work next week.

### Bond

B. Riggs-Project Manager




Knock down and compaction of import fill materials

## New Elementary - Eastpoint

This week, we've completed work on drilled piers and the detention pond is close to completion. Work continues on the underground plumbing and grade beam construction.

### Bond

B. Garcia—Project Inspector

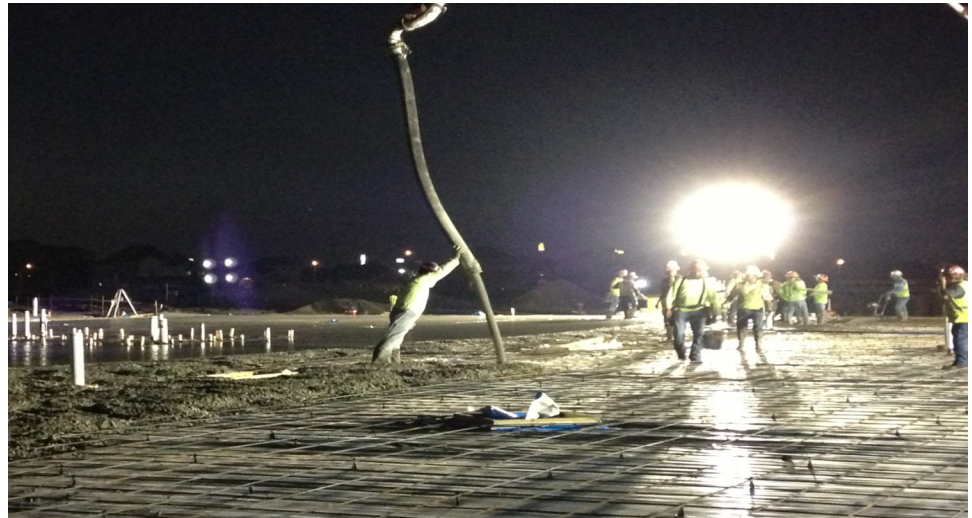

### Crockett Parking Lot and Drive

Work continues on the south drive entry. Gate posts for the new gates were set in the footings.

**Non Bond**

B. Garcia-Project Inspector



### Portable Classrooms-Hopper

Wiring for phones and intercom system should be complete this week.

**Non Bond**

T. Ortman-Project Inspector



### Robert E. Lee Parking Lot and Drive

All grading was completed and the parking area was compacted. Conduit work will begin soon for the installation of new light poles.

**Bond**

B. Garcia-Project Inspector



## BOND & NON BOND

Facilities Planning & Construction  
3401 N. Main  
Baytown, Texas 77521

Phone: 281-425-3600  
Fax: 281-420-5140  
E-mail: [dkfluker@gccisd.net](mailto:dkfluker@gccisd.net)

## Pending Projects

**Ross S. Sterling Athletic Parking** - Proposals opened on September 4th and are scheduled for board approval on September 23rd.

**Sterling; Ronnie Kluch Entrance**— Bids have been received and are being evaluated.

**Impact Early College High School** - Architectural qualifications are being evaluated and are scheduled for board approval on September 23nd.

