

Facilities Weekly Report

Volume II, Issue 8

Week of October 7-11, 2013

New Elementary - Hwy 146

Marshall Construction has drilled and installed all 340 building piers at this site.

Bond

R. Brown-Senior Project Inspector



Inside this issue:

New Elementary on Eastpoint 2

Hwy 146 Elementary School Groundbreaking 2

Crockett Parking Lot and Drive 3

Vent Hoods 3

Robert E. Lee Parking Lot and Drive 3

New Alamo Elementary - N. Main

Marshall Construction has started the concrete work in area "A," which will be the pre-k and 1st grade classrooms. They are also preparing to pour grade beams in area "C", which will be the administration area.

Bond

R. Brown-Senior Project Inspector




New Elementary - Eastpoint

Marshall Construction has completed the final concrete pour in area "D," which will be the 4th and 5th grade classrooms.

Bond

R. Brown-Senior Project Inspector

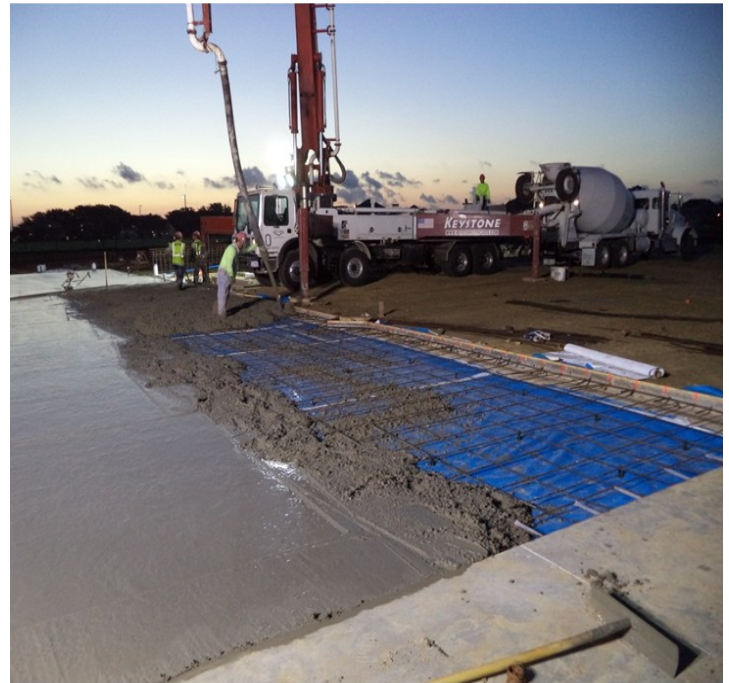

Hwy 146 Elementary Groundbreaking Ceremony

On Wednesday, many people from the school district, Board of Trustees, and the Baytown community gathered for the groundbreaking ceremony of the new elementary at Highway 146. Dr. Cavazos spoke of the importance of the Bond and building our new campuses, due to the growth of our community. Children were present, they recited the pledges, sang songs, and participated in imprinting their hands in concrete to commemorate the ceremony.

B. Garcia-Project Inspector



Crockett Parking Lot and Drive

The new extension of the north side parking lot was poured early in the week. The extension will provide thirty-one additional parking spaces. A portion of the new parent drive, beginning at the Barkaloo end, was formed and is ready for a concrete pour early next week.

Non Bond

B. Garcia-Project Inspector



Vent Hoods

The vent hood installation process has begun. Formica and hardware has been matched at Harlem, DeZavala, Highlands and Austin Elementary Schools. Dimensions were also taken in preparation for the vent hoods.

Non Bond

T. Ortman-Project Inspector



Robert E. Lee Parking Lot and Drive

Trenching for the new parking lot lights continued this week on the other half of the lot. Conduit was laid and the new trenching was inspected and partially covered.

Bond

B. Garcia-Project Inspector



BOND & NON BOND

Facilities Planning & Construction
3401 N. Main
Baytown, Texas 77521

Phone: 281-425-3600
Fax: 281-420-5140
E-mail: dkfluker@gccisd.net

Pending Projects

Ross S. Sterling North Parking - This project was taken before the Board for approval on September 23, 2013. Currently, we are in negotiations for a contract with G. W. Phillips.

Sterling; Ronnie Kluch Entrance- We are re-advertising for proposals. The price requests resulted in "no Bids" received.

Impact Early College High School - The Contract with PBK is going before the Board of Trustees on October 14 for their approval.

