

# Facilities Weekly Report

Volume II, Issue 9

Week of October 14-18, 2013

## New Elementary - Hwy 146

Marshall Construction is putting in partial grade beam poured Pre-K and 1st grade classroom areas. Also sanitary sewer main being installed.

### Bond

R. Brown-Senior Project Inspector



### Inside this issue:

New Elementary on Eastpoint 2

Hwy 146 Elementary School Groundbreaking 2

Crockett Parking Lot and Drive 3

Vent Hoods 3


Robert E. Lee Parking Lot and Drive 3

## New Alamo Elementary - N. Main

Marshall Construction has started the concrete work in the 4th and 5th grade classrooms and restrooms areas, Approximately 33,000 SF of concrete poured.

### Bond

R. Brown-Senior Project Inspector

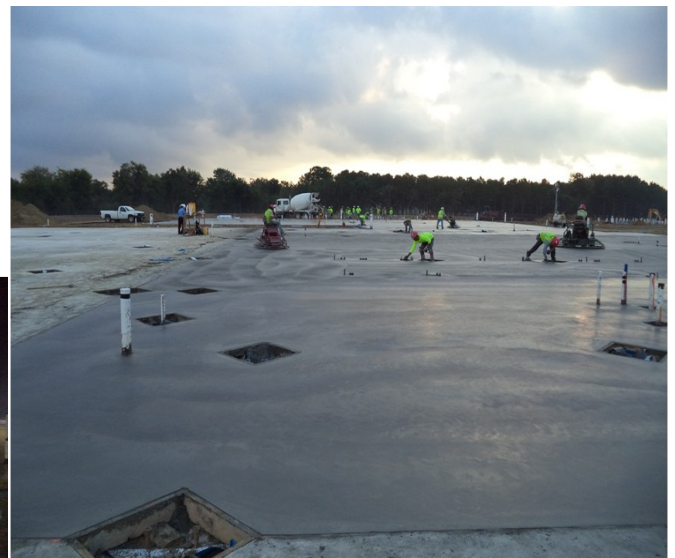

## New Elementary - Eastpoint

Marshall Construction has spread lime stabilization of Sub-grade for Visitors parking pavement and preparing for thickened slab in PE, Cafeteria and Stage areas. Structural steel erection commences.

### Bond

R. Brown-Senior Project Inspector



## Crockett Parking Lot and Drive

The new extension of the north side parking lot was poured early in the week. The extension will provide thirty-one additional parking spaces. A portion of the new parent drive, beginning at the Barkaloo end, was formed and is ready for a concrete pour early next week.

### Non Bond

B. Garcia-Project Inspector



## Vent Hoods

The vent hood installation process has begun. Formica and hardware has been matched at Harlem, DeZavala, Highlands and Austin Elementary Schools. All materials have been ordered. Contractor has begun building the cabinets to prepare for the new vent hoods.

### Non Bond

T. Ortman-Project Inspector



## Robert E. Lee Parking Lot and Drive

Horizon is trenching for the new parking lot lights continued this week on the other half of the lot. Conduit was laid and the new trenching was inspected and partially covered. Reinforcing steel for the paving has been delivered to the site.

### Bond

B. Garcia-Project Inspector



## BOND & NON BOND

Facilities Planning & Construction  
3401 N. Main  
Baytown, Texas 77521

Phone: 281-425-3600  
Fax: 281-420-5140  
E-mail: [dkfluker@gccisd.net](mailto:dkfluker@gccisd.net)

## Pending Projects

**Ross S. Sterling North Parking** - This project was taken before the Board for approval on September 23, 2013. Currently, we are in negotiations for a contract with G. W. Phillips.

**Sterling; Ronnie Kluch Entrance**- We are re-advertising for proposals. The price requests resulted in "no Bids" received.

**Impact Early College High School** - The Contract with PBK was approved by the Board of Trustees on October 14.

